



Northfield City Council Meeting

November 7, 2023


AGENDA



- » City Build Status
- » Construction Communication
- » Community Commitment
- » Wrap Up & Questions

CITY BUILD STATUS

- » What Is Completed To Date
 - » 3,949 passes
 - » 288,711 feet of underground
 - » 50,932 feet of aerial
- » What Is Remaining
 - » 594 passes
 - » 750 feet of underground
 - » 0 feet of aerial
- » Estimate to Completion
 - » May 17, 2024

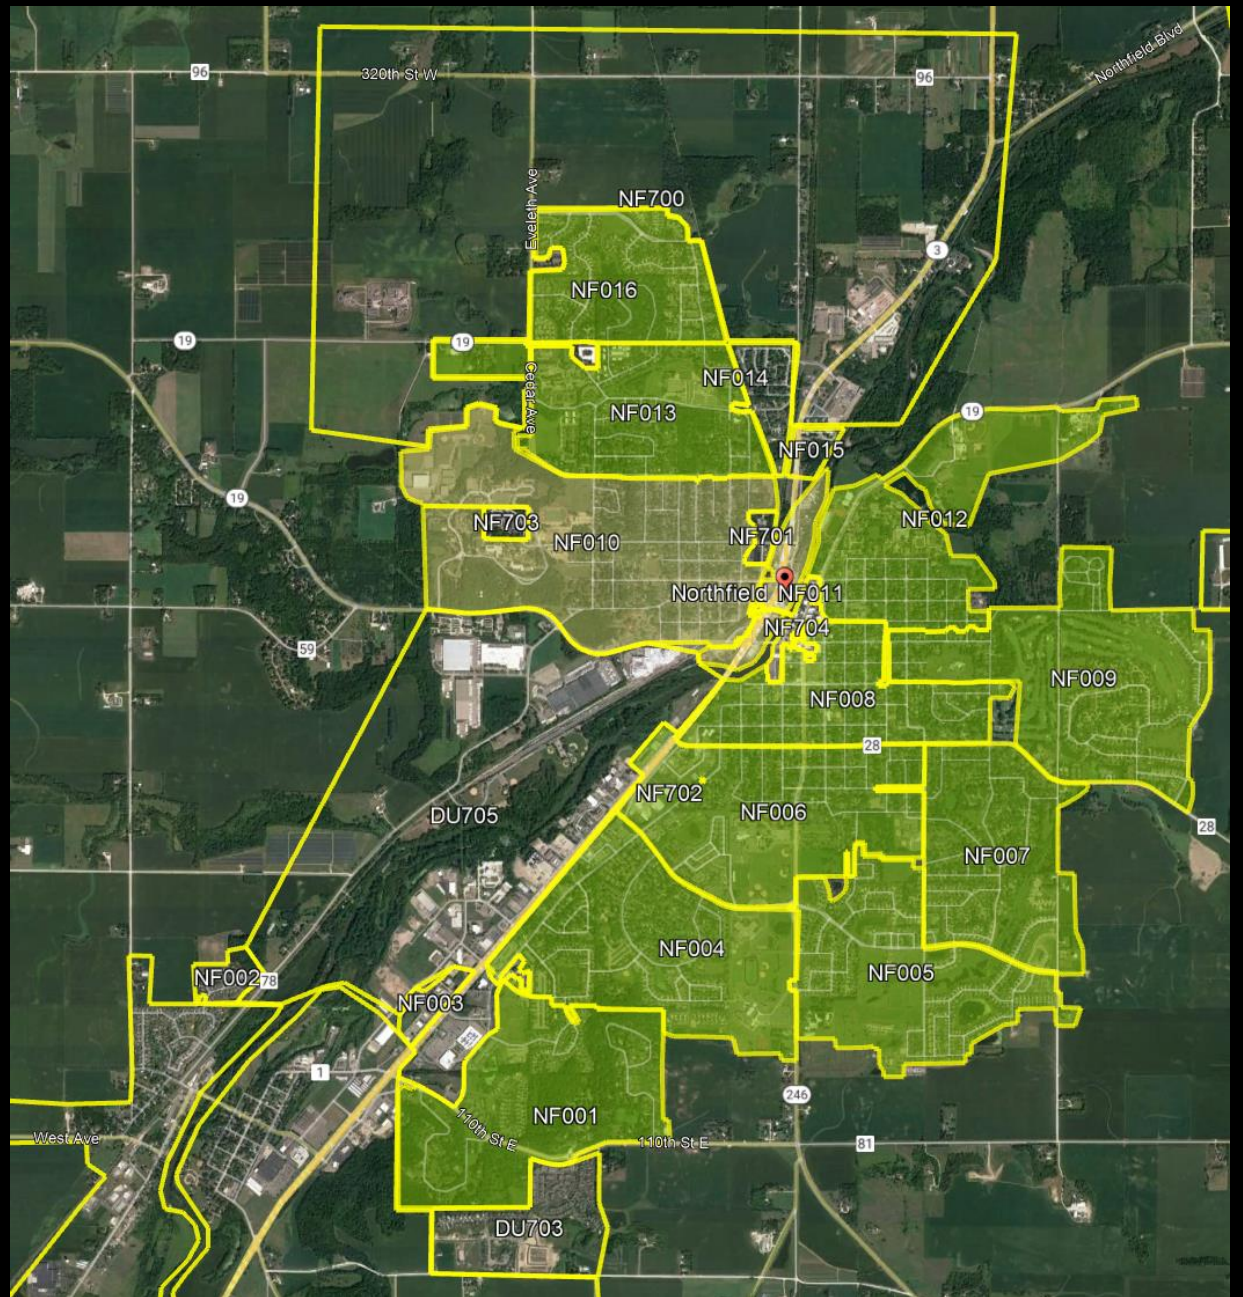

CONSTRUCTION COMMUNICATION (tickets)

» Responsiveness

» 99%+ response rate within 24 hrs.


» Completion

» 98%+ completed within 7 days



	Total Tickets	209
52%	Completed within 24 Hours	108
33%	Completed within 1-3 Days	68
10%	Completed within 4-7 Days	21
1%	Completed in 8+ Days	3
0%	On Hold	0
<1%	In Progress	1
4%	Cancelled	8

Ticket Type	Cancelled	Closed	In Progress	Grand Total
Cable Line		3		3
Customer Damage	2	35		37
Electric Line		1		1
Notification	4	112	1	117
Phone Line		2		2
Restoration	2	47		49
Grand Total	8	200	1	209

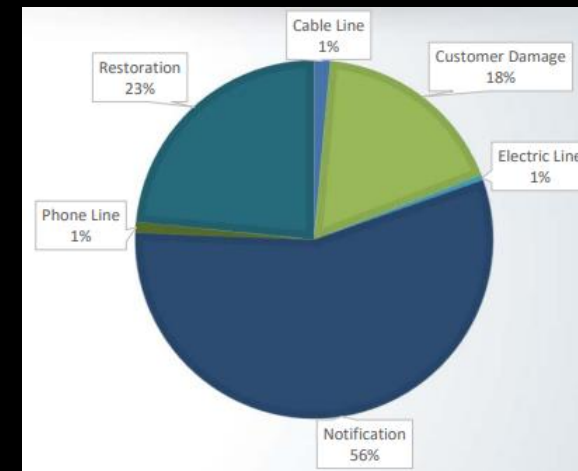

COMMUNITY DEVELOPMENT

» HOAs, Townhomes, Condos, Manufactured Home Parks, Residential Expansions

Examples:

- Northfield Townhomes
- Prairie Hills Townhomes
- Spring Creek Townhomes
- Viking Terrace
- Riverview
- Erie Drive expansion
- Lincoln Woods expansion



COMMUNITY ENGAGEMENT

» Events, Sponsorships, Volunteering,
Chamber Outings

Examples:

- Community Market Fair
- Defeat of Jesse James Days
- Winter Walk



Wrap Up



- » Multi-million investment solely funded by Metronet (no public, city, state or federal funds)
- » 32 month city build (10/2021 to 5/2024)
- » Majority of residents & businesses have access to multi-gig symmetrical service
- » Questions

metronetTM

Craig Zimmerman
Government Affairs Manager
(515) 689-8792
Craig.Zimmerman@metronet.com

Toby Brummer
Outside Plant Project Director
(507) 450-7757
Toby.Brummer@metronet.com
